

666176 1/2 x W.045

Work Order ID 153788

153788

Page 1

Friday, November 25, 2016 7:43:07 AM

Item ID: D3504-1 Accept *N900040100* Setup Start *NS1*
 Revision ID: Stop *NS2*
 Item Name: Crossbolt Spacer
 Start Date: 11/28/2016 Start Qty: 6.00 *6* Cust Item ID:
 Required Date: 12/5/2016 Req'd Qty: 6.00 *6* Customer:
 Reference:

Approvals: Process Plan: DAS 21 9-89 Date: NOV 29 2016 Tooling: _____ Date: _____ Run Start *NR1*
 QC: _____ Date: _____ SPC (Y/N): _____ Date: _____ Stop *NR2*

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
--------------------------------	--------------------------	----------------------	---------	--------	--------------	---------------	---------------	------------------	----------------

Draw Nbr	Revision Nbr
D3504	Rev C

100	Hardinge CNC LATHE SMALL	0.00				19	0		DAS 45 9-89 17-01-08
-----	--------------------------	------	--	--	--	----	---	--	----------------------

100
 Hardinge
 Hardinge CNC Lathe Small
 Memo
 1-TURN AS PER FOLIO FA642 & DWG D3504 ,
 FOLIO REV: FA
 DWG REV: C
 2-DEBURR AS REQUIRED

110	QC2- Inspect parts off machine FAI/FAIB	0.00				19	0		DAS 45 9-89 17-01-08
-----	---	------	--	--	--	----	---	--	----------------------

110
 QC
 Quality Control
 Memo

120	QC8- Inspect parts - second check	0.00				19	0		DAS 14 9-89 17/01/09
-----	-----------------------------------	------	--	--	--	----	---	--	----------------------

120
 QC
 Quality Control
 Memo

DQA: _____ Date: _____

WORK ORDER NON-CONFORMANCE / UPDATE



QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐							
Date :		Step #:		QTY Effective :				MRB (QSI042) Approval Completed By Lead hand / Supervisor Approval Verification QC / QA Coordinator Approval			
Description Work Order Deviation				Disposition							
Root Cause Environment ☐ No Re-verification ☐ Design ☐ Operator ☐ Doc/Data ☐ Offset/Setup ☐ Equip/Tooling ☐ Supplier ☐ Handling/Pre ☐ Training ☐ Material ☐ Use for Testing ☐ Internal Transport ☐ Poor Information ☐ Tribal Knowledge ☐ Rushing ☐ LOA ☐ Product Improvement ☐ Substation ☐ Process Improvement ☐ Past Expiry Date ☐ Manufacturing Process ☐ Misidentified ☐ Past Due ☐		Pressure/Forced ☐ Temperature/Cure ☐ Bending ☐ Set-up ☐ Centre Not Concentric ☐ BOM/Route ☐ Cracks ☐ Broken/Damage/Defect ☐ Crimp/Kink/Ripple/Wave ☐ Inspection Incomplete/Unqualified ☐ Cuffs ☐ Contamination ☐ Crushing ☐ Countersink ☐ Heat Treat ☐ Cut Too Short ☐ Wave/Twist in Tube ☐ Instructions Incomplete/Unclear ☐ Marks/Chatter ☐ Drill Holes ☐ Power Loss/Surge ☐ Positioned Wrong ☐ Folio/Program ☐ Outside Dimensions ☐ Grain ☐ Over/Under tolerance ☐ Weld ☐ Part Incorrect ☐ Wrong Stock Pulled ☐ Part Lost/Missing ☐ Out of Sequence ☐ Part Moved ☐ Off-set ☐ Drawing ☐ Misabeled ☐ Finish ☐ Fit/Function ☐ Misread ☐ Misaligned/off center ☐ Turning Sequence ☐									
OTHER : _____											

Work Order ID 153788

Friday, November 25, 2016 7:43:07 AM

153788

Page 2

Item ID: D3504-1

Accept

N900040100

Setup Start

NS1

Revision ID:

Stop

NS2

Item Name: Crossbolt Spacer

Start Date: 11/28/2016 Start Qty: 6.00

6

Cust Item ID:

Required Date: 12/5/2016 Req'd Qty: 6.00

6

Customer:

Reference:

Approvals:

Process Plan: _____

Date: _____

Tooling: _____

Date: _____

Run Start

NR1

QC: _____

Date: _____

SPC (Y/N): _____

Date: _____

Stop

NR2Sequence ID/
Work Center IDOperation
DescriptionSet Up/
Run Hours

Tool ID

Tool #

Plan
CodeAccept
QtyReject
QtyReject
NumberInsp.
Stamp

130

Identify as per dwg & Stock Location: LG001

0.00


130

Packaging

Memo

0.00

Packaging

STOCK IN SKIDTUBE CELL
LOCATION : LG00119 17-01-09


140

QC21- Final Inspection - Work Order Release

0.00

140

QC

Memo

0.00

Quality Control

DAS
21
9-89

JAN 10 2017

mf
17-01-09

DQA: _____ Date: _____

WORK ORDER NON-CONFORMANCE / UPDATE



QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :				MRB (QSI042) Approval 	
Description Work Order Deviation				Disposition					
								Completed By	
								Lead hand / Supervisor Approval Verification	
								QC / QA Coordinator Approval	

Root Cause				FAULT CATEGORY							
Environment	☐	No Re-verification	☐	Pressure/Forced	☐	Temperature/Cure	☐	Power Loss/Surge	☐	Positioned Wrong	☐
Design	☐	Operator	☐	Bending	☐	Set-up	☐	Folio/Program	☐	Outside Dimensions	☐
Doc/Data	☐	Offset/Setup	☐	Centre Not Concentric	☐	BOM/Route	☐	Grain	☐	Over/Under tolerance	☐
Equip/Tooling	☐	Supplier	☐	Cracks	☐	Broken/Damage/Defect	☐	Weld	☐	Part Incorrect	☐
Handling/Pre	☐	Training	☐	Crimp/Kink/Ripple/Wave	☐	Inspection Incomplete/Unqualified	☐	Wrong Stock Pulled	☐	Part Lost/Missing	☐
Material	☐	Use for Testing	☐	Cuffs	☐	Contamination	☐	Out of Sequence	☐	Part Moved	☐
Internal Transport	☐	Poor Information	☐	Crushing	☐	Countersink	☐	Off-set	☐	Drawing	☐
Tribal Knowledge	☐	Rushing	☐	Heat Treat	☐	Cut Too Short	☐	Mislabeled	☐	Finish	☐
LOA	☐	Product Improvement	☐	Wave/Twist in Tube	☐	Instructions Incomplete/Unclear	☐	Fit/Function	☐	Misread	☐
Substation	☐	Process Improvement	☐	Marks/Chatter	☐	Drill Holes	☐	Misaligned/off center	☐	Turning Sequence	☐
Past Expiry Date	☐	Manufacturing Process	☐	OTHER : _____							
Misidentified	☐	Past Due	☐								

Picklist Print

Friday, November 25, 2016 7:43:07 AM

Page 1
/

Work Order ID: 153788

153788

Parent Item: D3504-1

D3504-1

Parent Item Name: Crossbolt Spacer

Start Date: 11/28/2016

Required Date: 12/5/2016

Start Qty: 6.00

Required Qty: 6.00

Comments: IPP Rev:A New Issue 06-06-20 JLM
IPP Rev:B Rev C dwg 07-12-06 DD verified by:EC

Component Item ID/ Item Name	Replacement Item ID	Mfg/ Purch	Bin Item	Primary Location	Last Location	Route Seq ID	Unit of Measure	Qty on Hand	Qty per Kit	Total Qty	Qty Issued	Date Issued	Status
M6061T6T0.500W.049		Purchased				100	f	183.9950	0.283	1.787368			

M6061T6T0 500W 049

6061-T6 RD Tube .500 x.049W

Location

Loc Qty

Loc Code

MAT013

183.995

m131932

183.995

6.0 ^{DAS}
⁴⁵ 17-01-08
⁹⁻⁸⁹

DQA: _____ Date: _____


WORK ORDER NON-CONFORMANCE / UPDATE



QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval 		
Description Work Order Deviation				Disposition					
							Completed By		
							Lead hand / Supervisor Approval Verification		
							QC / QA Coordinator Approval		
Root Cause		FAULT CATEGORY							
Environment ☐	No Re-verification ☐	Pressure/Forced ☐	Temperature/Cure ☐	Power Loss/Surge ☐	Positioned Wrong ☐				
Design ☐	Operator ☐	Bending ☐	Set-up ☐	Folio/Program ☐	Outside Dimensions ☐				
Doc/Data ☐	Offset/Setup ☐	Centre Not Concentric ☐	BOM/Route ☐	Grain ☐	Over/Under tolerance ☐				
Equip/Tooling ☐	Supplier ☐	Cracks ☐	Broken/Damage/Defect ☐	Weld ☐	Part Incorrect ☐				
Handling/Pre ☐	Training ☐	Crimp/Kink/Ripple/Wave ☐	Inspection Incomplete/Unqualified ☐	Wrong Stock Pulled ☐	Part Lost/Missing ☐				
Material ☐	Use for Testing ☐	Cuffs ☐	Contamination ☐	Out of Sequence ☐	Part Moved ☐				
Internal Transport ☐	Poor Information ☐	Crushing ☐	Countersink ☐	Off-set ☐	Drawing ☐				
Tribal Knowledge ☐	Rushing ☐	Heat Treat ☐	Cut Too Short ☐	Mislabeled ☐	Finish ☐				
LOA ☐	Product Improvement ☐	Wave/Twist in Tube ☐	Instructions Incomplete/Unclear ☐	Fit/Function ☐	Misread ☐				
Substation ☐	Process Improvement ☐	Marks/Chatter ☐	Drill Holes ☐	Misaligned/off center ☐	Turning Sequence ☐				
Past Expiry Date ☐	Manufacturing Process ☐	OTHER : _____							
Misidentified ☐	Past Due ☐								

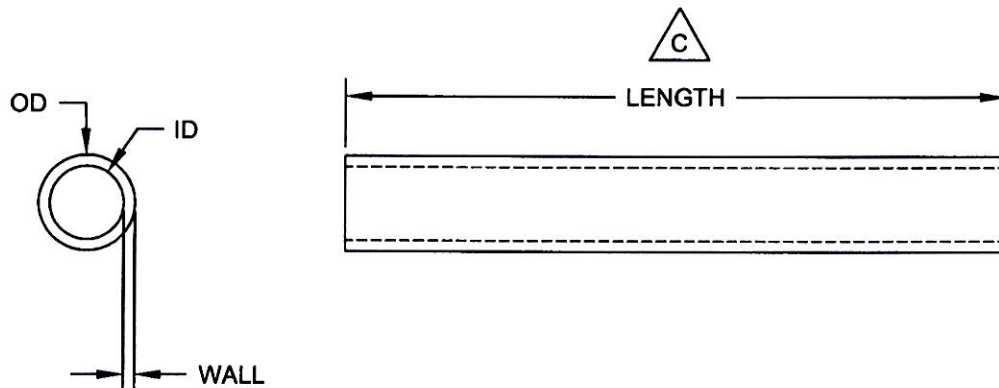

SHOP COPY
 RETURN TO
 ENGINEERING
 UNCONTROLLED COPY
 SUBJECT TO AMENDMENT
 WITHOUT NOTICE
 WORK ORDER
 NO. 153788 M0394
 16-11-2016

D3504-1/-3/-5 CROSS BOLT SPACER PARTS LIST

PART NUMBER	OD	WALL	LENGTH +0.030 -0.000	ID	MATERIAL SPEC	NOTE
D3504-1	0.500	0.049	3.475	0.402 (REF)	M6061T6T0.500W.049	SEE NOTE 1a)
D3504-3	0.375	0.049	3.475	0.277 (REF)	M6061T6T0.375W.049	SEE NOTE 1a)
D3504-5	0.750	0.080 (REF)	3.400	0.590	M6061T6R0.750	SEE NOTE 1b)



D3504-1/-3/-5 CROSS BOLT SPACER:

- 1) MATERIAL: a) 6061-T6 OR 6061-T62 TUBING
 PER WW-T-700/6 OR AMS 4080 OR AMS 4082
 OR QQ-A-200/8 OR QQ-A-225/8
 (REF. DART SPEC. M6061T6TD.DDDW.TTT)
- b) 6061-T6 (OR 6061-T651/T6510/T6511/T62) ROUND BAR
 PER AMS-QQ-A-225/8 (OR AMS 4117/4128/4115/4116) OR
 PER AMS-QQ-A-200/8 (OR AMS 4160)
 (REF. DART SPEC. M6061T6R0.750)
- 2) FINISH: NONE
- 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED
- 5) BREAK SHARP EDGES: 0.005 TO 0.010 MAX
- 6) IDENTIFICATION: NONE
- 7) WEIGHT: N/A

RELEASED

07.11.16

C	ADD -5	DC	07.09.19
B	3.475 WAS 3.400	PH	06.11.01
A	NEW ISSUE	PH	06.04.21
REV.	DESCRIPTION	BY	DATE
DESIGN	PH	DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA	
DRAWN	BC		
CHECKED	PH	DRAWING NO.	REV. C
MFG. APPR.	BC	D3504	SHEET 1 OF 1
APPROVED	PH	TITLE	SCALE
DE APPR.	PH	CROSS BOLT SPACER	NTS
DATE	07.09.19	COPYRIGHT © 2006 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.	
